



# Lago Vista ISD Monthly Construction Update April 2022




**Lockwood, Andrews  
& Newnam, Inc.**  
A LEO A DALY COMPANY



**Huckabee**

**WEAVER & JACOBS**  
CONSTRUCTORS, INC.

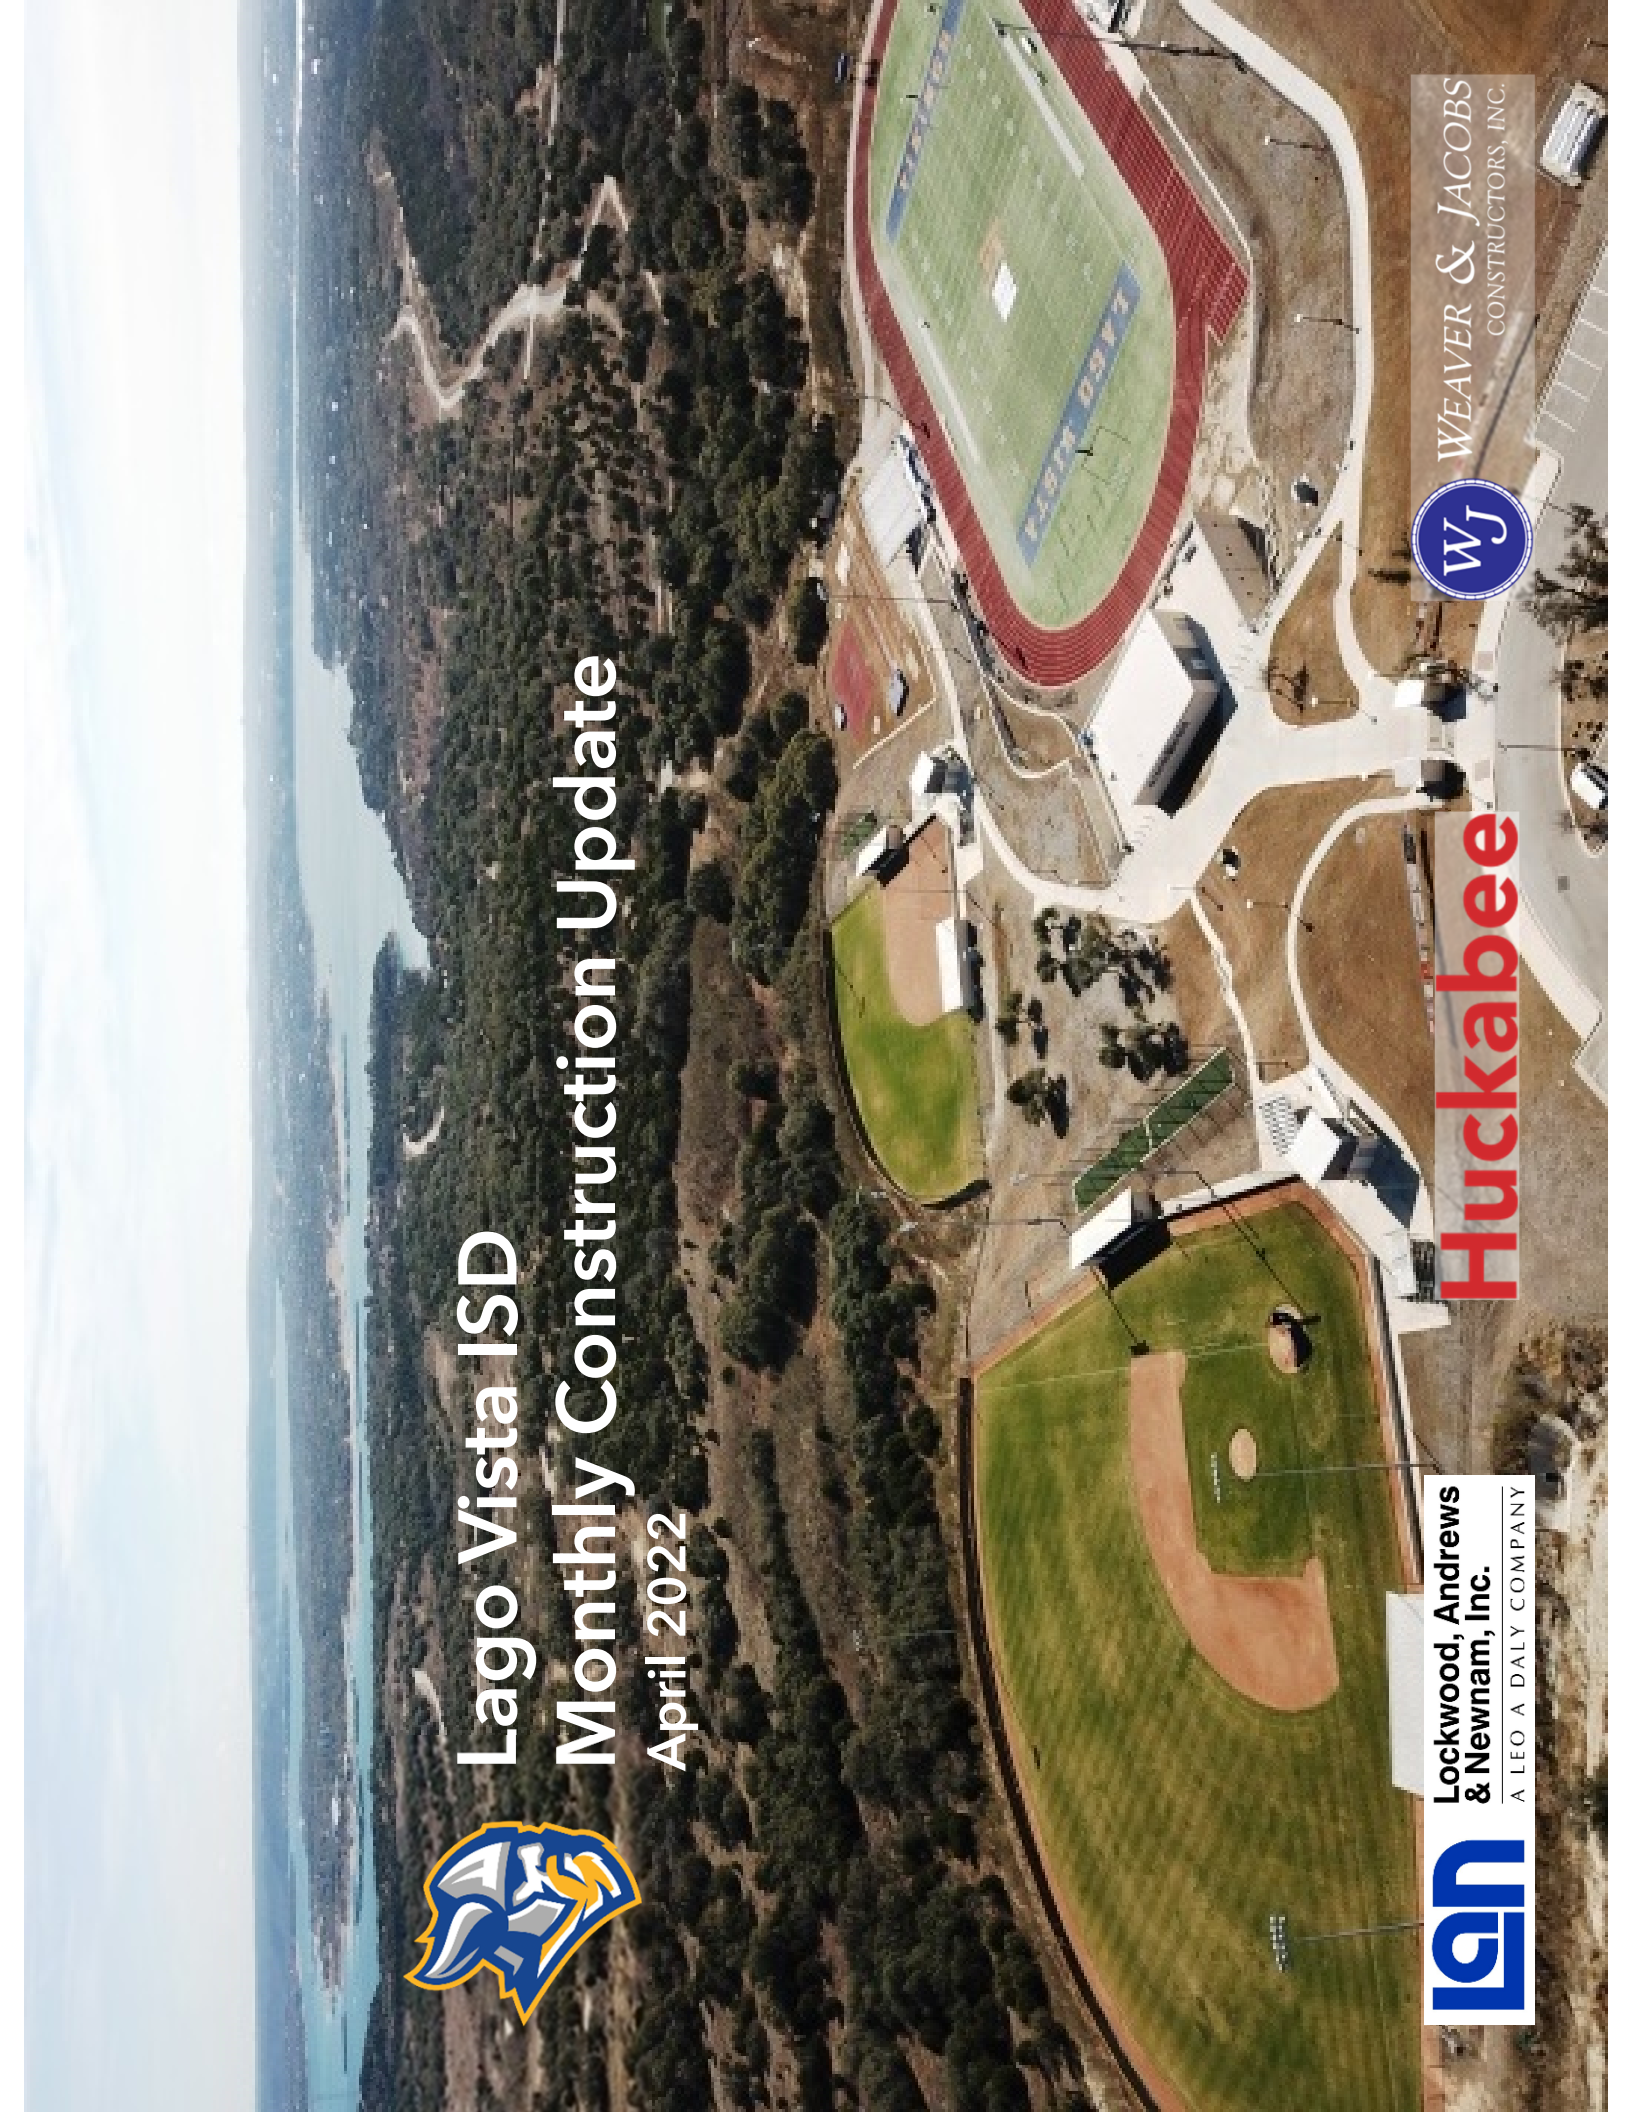



# Lago Vista ES Master Schedule



Activity	2021	2022	2023							
	Aug	Oct	Dec	Jan	Feb	Apr	Jun	Aug	Oct	Dec
Admin Reno						Today		Planned May 25	Planned Aug 8	
Café Addition										
Library Addition										
Classroom Addition										
Site Work										

Budget	Committed	Expenditures	Unencumbered
\$17,510,265	\$16,959,418	\$7,492,657	\$550,847





# Lago Vista Elementary School Additions/Renovations



Classroom Addition Exterior



Classroom Addition Exterior




Classroom Addition Interior



Cafeteria Addition



# Lago Vista HS Master Schedule

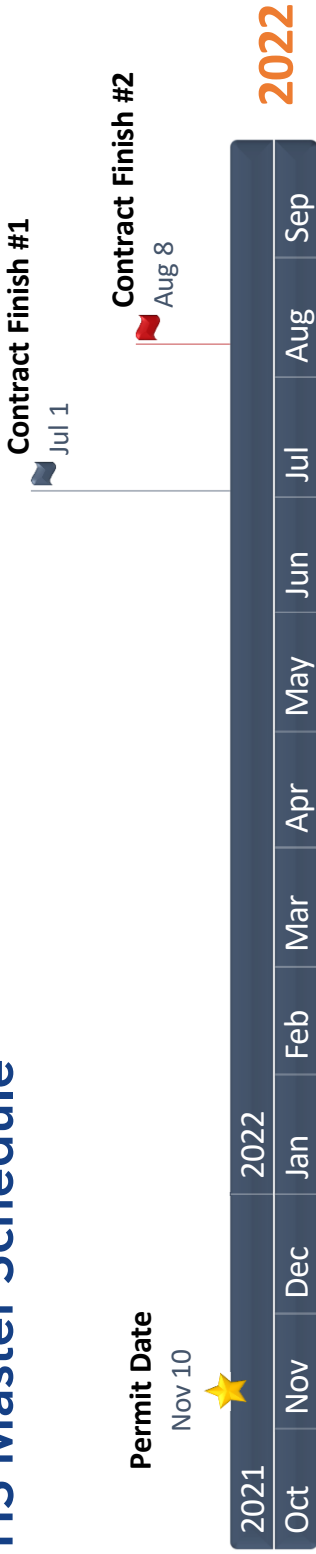

2021

2022

Project	Actual Start	Planned	Forecast Finish
HSci/Culinary Addition	Oct 18	Planned	Forecast Finish Jul 6
Cafe Addition		Planned	Forecast Finish Aug 8
Shop/Weight Room Addition	Oct 18	Planned	Forecast Finish Sep 20
Locker Room Reno		Planned	Forecast Finish Aug 8
Fine Arts Addition	Oct 18	Planned	Forecast Finish Aug 9
Sitework	Actual Start Dec 27	Planned	Forecast Finish Aug 18

Budget	Committed	Expenditures	Unencumbered
\$11,112,764	\$10,510,452	\$3,812,200	\$602,312





# Lago Vista High School Additions



Health Science/Culinary Arts Addition



Shop/Weight Room Addition



Fine Arts Addition



Shop/Weight Room Addition



# Lago Vista MS Master Schedule

Contract Finish #1  
Jul 15

Contract Finish #2  
Oct 25

Permit Date  
Mar 2



2021

2022

2023

2023

Activity	2021 Oct	2021 Dec	2022 Feb	2022 Apr	2022 Jun	2022 Aug	2022 Oct	2022 Dec	2023 Feb	2023 Apr
Science Labs Renovation										
Hallway Renovation					RePlanned May 30 Jun 17					
New Addition										
Sitework										
Courtyard										
Cooling Tower										

Budget	Committed	Expenditures	Unencumbered
\$8,773,167	\$8,345,973	\$1,759,218	\$427,194
