



Lago Vista ISD Monthly Construction Update August 2023



**Lockwood, Andrews
& Newnam, Inc.**
A LEO A DALY COMPANY

Huckabee



WEAVER & JACOBS
CONSTRUCTORS, INC.



Lago Vista 2020 Bond Program Financial Summary

Project Financial Summary

Project	Budget	Committed	Expenditures	Unencumbered
LVES	\$17,155,844.92	\$16,937,047.47	\$16,666,385.42	\$218,797.45
LVHS	\$10,957,376.58	\$10,612,748.57	\$10,553,919.68	\$344,628.01
LVIS	\$3,966,154.89	\$584,069.07	\$176,592.74	\$3,382,085.82
LVMS	\$8,741,981.81	\$8,544,812.29	\$8,234,493.86	\$197,169.52
LVMS-Roof	\$1,862,230.00	\$1,847,114.50	\$1,847,114.50	\$15,115.50
Real Estate/PM	\$1,646,411.80	\$822,242.71	\$818,895.07	\$824,169.09
Grand Total	\$44,330,000.00	\$39,348,034.61	\$38,297,401.27	\$4,981,965.39

89% of Budget

97% of Committed

11% of Budget

Project Allowances Summary

Project	Beginning Balance	Revised Balance	Approved	Pending	Remaining Balance
LVES	\$442,750.00	\$670,592.27	\$522,975.27	\$147,617.00	\$0
LVHS	\$277,211.00	\$265,362.44	\$265,362.44	\$0	*\$0
LVMS	\$235,750.00	\$375,750.00	\$178,113.70	\$172,669.00	\$24,967.30
Grand Total	\$955,711.00	\$1,311,704.71	\$966,451.41	\$320,286.00	\$24,967.30

* Note: Remaining unused balance transferred to Elementary School Project



Lago Vista 2020 Bond Program Work Progress Summary

Middle School

- Final interior door installation in progress
- Some doors found to be without complete hardware
- Room signs not complete
- Plumbing fixtures are in progress
- Toilet partitions not started
- Classroom floors are waxed but need to be cleaned
- Wall outlet and other equipment boxes need to be closed up
- Exterior wall finish at courtyard is in progress
- Some exit signs are still in progress
- Some floor tiles require replacement
- Corridor wainscot tile requires grouting in some places
- Corridor egress lighting not complete
- Damaged ceiling tile needs replacement
- HVAC Final Inspection - Friday, August 4th
- Plumbing/Electrical/Fire Alarm Final Inspection - Tuesday, August 8th
- Occupancy Final Inspection - Wednesday, August 9th

Elementary School & High School Interior Warranty Walk

- Scheduled for Wednesday, August 9



Lago Vista MS Addition/Renovations



Science Wing Main Entrance Corridor



Lago Vista MS Addition/Renovations



Courtyard- Prep for Exterior Stucco Work




Lago Vista MS Addition/Renovations



Science Lab



Lago Vista MS Addition/Renovations

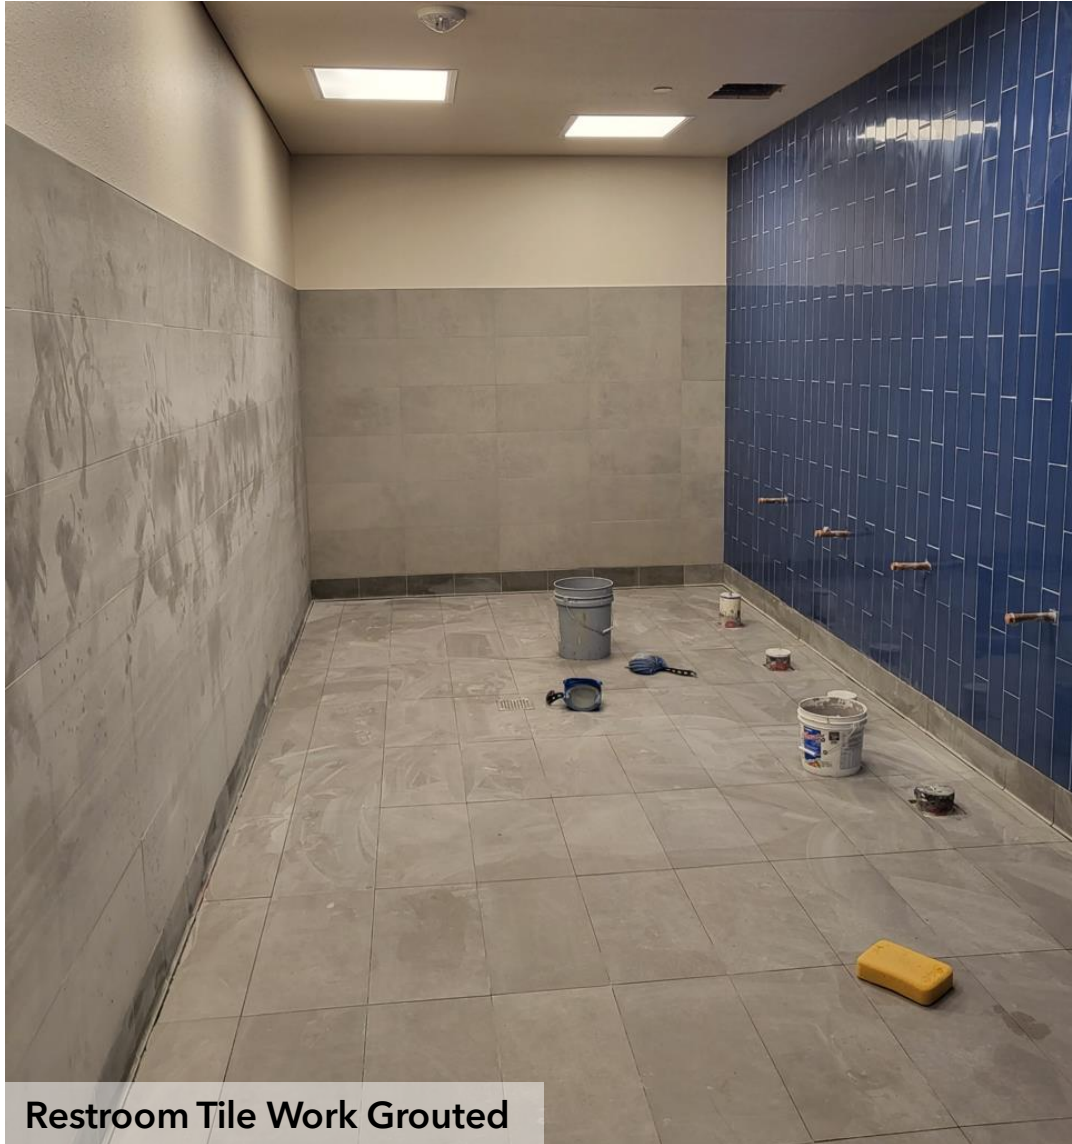

Restroom Tile Work Grouted



Lago Vista ISD Monthly Construction Update August 2023



**Lockwood, Andrews
& Newnam, Inc.**
A LEO A DALY COMPANY

Huckabee



WEAVER & JACOBS
CONSTRUCTORS, INC.
