



Lago Vista ISD Monthly Construction Update June 2022



**Lockwood, Andrews
& Newnam, Inc.**
A LEO A DALY COMPANY

Huckabee



WEAVER & JACOBS
CONSTRUCTORS, INC.



Lago Vista ES Master Schedule

Key Completions in June (Classroom Wing)

- HVAC Startup
- Finish Plumbing
- Electrical Trim Out
- Doors and Hardware




Budget	Committed	Expenditures	Unencumbered
\$17,510,265	\$16,959,418	\$9,567,162	\$550,847



Lago Vista Elementary School Additions/Renovations



Classroom Addition Exterior

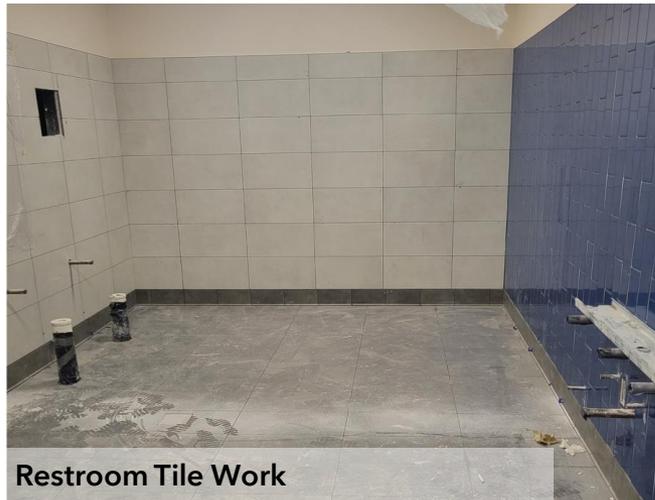

Restroom Tile Work



Classroom Wing Corridor



Cafeteria Addition




Lago Vista HS Master Schedule

- Key Completions in June**

 - Culinary/Fine Arts
 - HVAC Startup
 - Fine Arts
 - HVAC Startup
 - Shop/Weight Room
 - Permanent Power

Contract Finish #1
 Jul 1



Contract Finish #2
 Aug 8

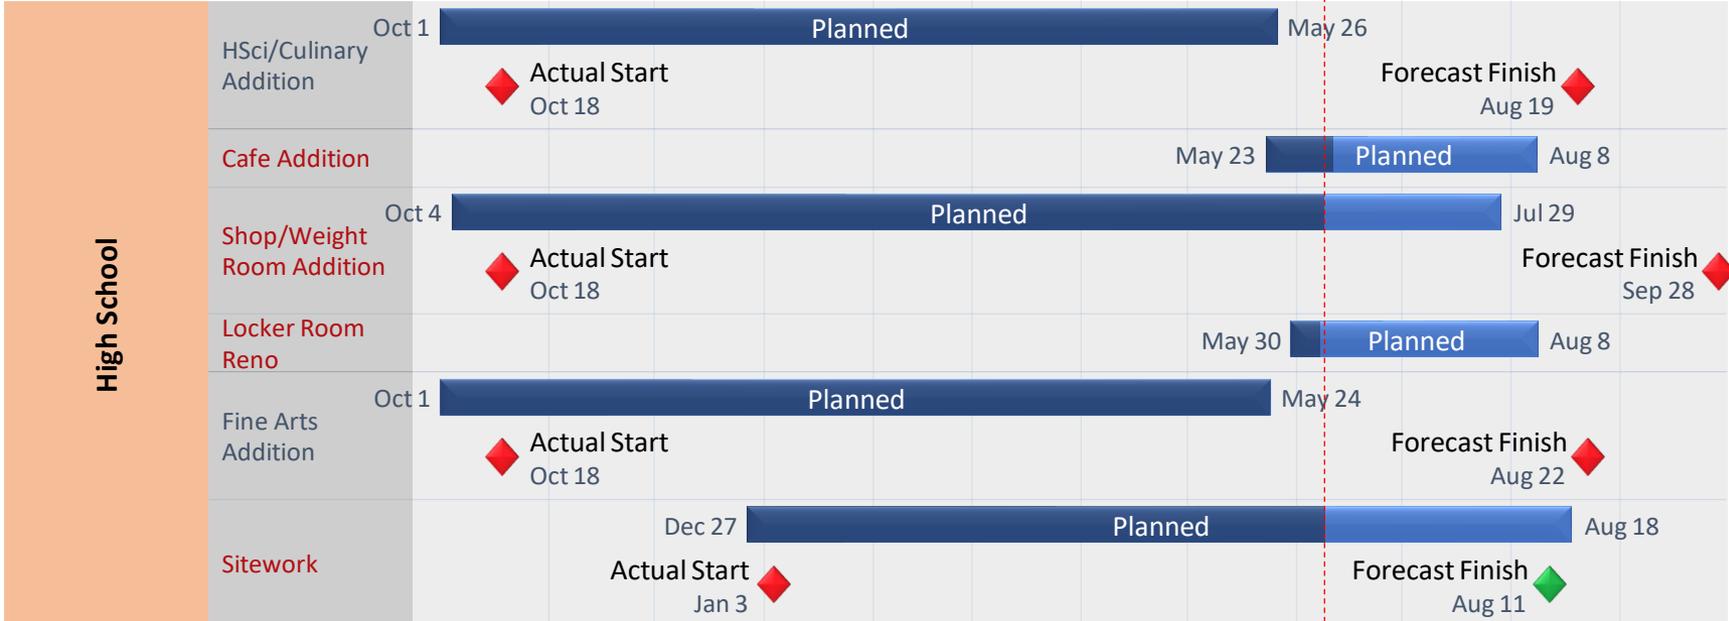

Budget	Committed	Expenditures	Unencumbered
\$11,112,764	\$10,510,452	\$5,487,513	\$602,312




Lago Vista High School Additions

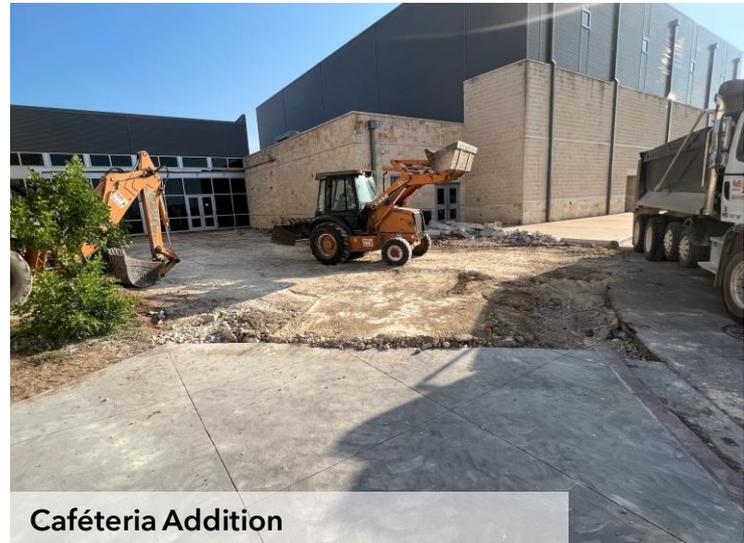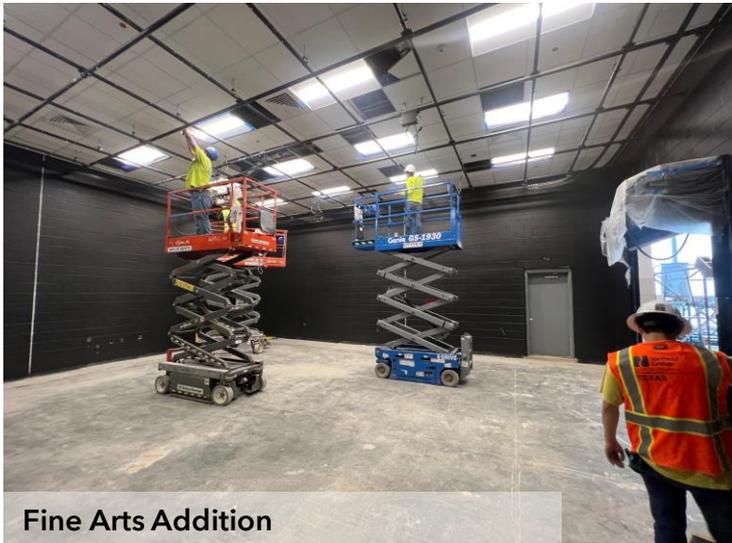



Lago Vista MS Master Schedule

2021



2023

Today



Middle School

Budget	Committed	Expenditures	Unencumbered
\$8,773,167	\$8,345,973	\$2,874,725	\$427,194



Lago Vista Middle School Addition and Renovations



Weight Room/Classroom Addition Exterior



Lobby Between Addition and Existing Building



Weight Room/Classroom Addition Interior



Weight Room/Classroom Addition Exterior



Lago Vista ISD Monthly Construction Update May 2022



**Lockwood, Andrews
& Newnam, Inc.**
A LEO A DALY COMPANY

Huckabee



WEAVER & JACOBS
CONSTRUCTORS, INC.
