



Lago Vista ISD Monthly Construction Update March 2022



**Lockwood, Andrews
& Newnam, Inc.**
A LEO A DALY COMPANY


Huckabee



WEAVER & JACOBS
CONSTRUCTORS, INC.



Lago Vista ES Master Schedule



Elementary School	Admin Reno					May 25	Planned	Aug 8			
	Café Addition	Sep 21					Planned			Jul 15	
	Library Addition										
	Classroom Addition	Sep 6						Planned			Jul 21
	Site Work										

Budget	Committed	Expenditures	Unencumbered
\$17,510,265	\$16,959,418	\$4,724,259	\$550,847





Lago Vista Elementary School Additions/Renovations






Lago Vista HS Master Schedule

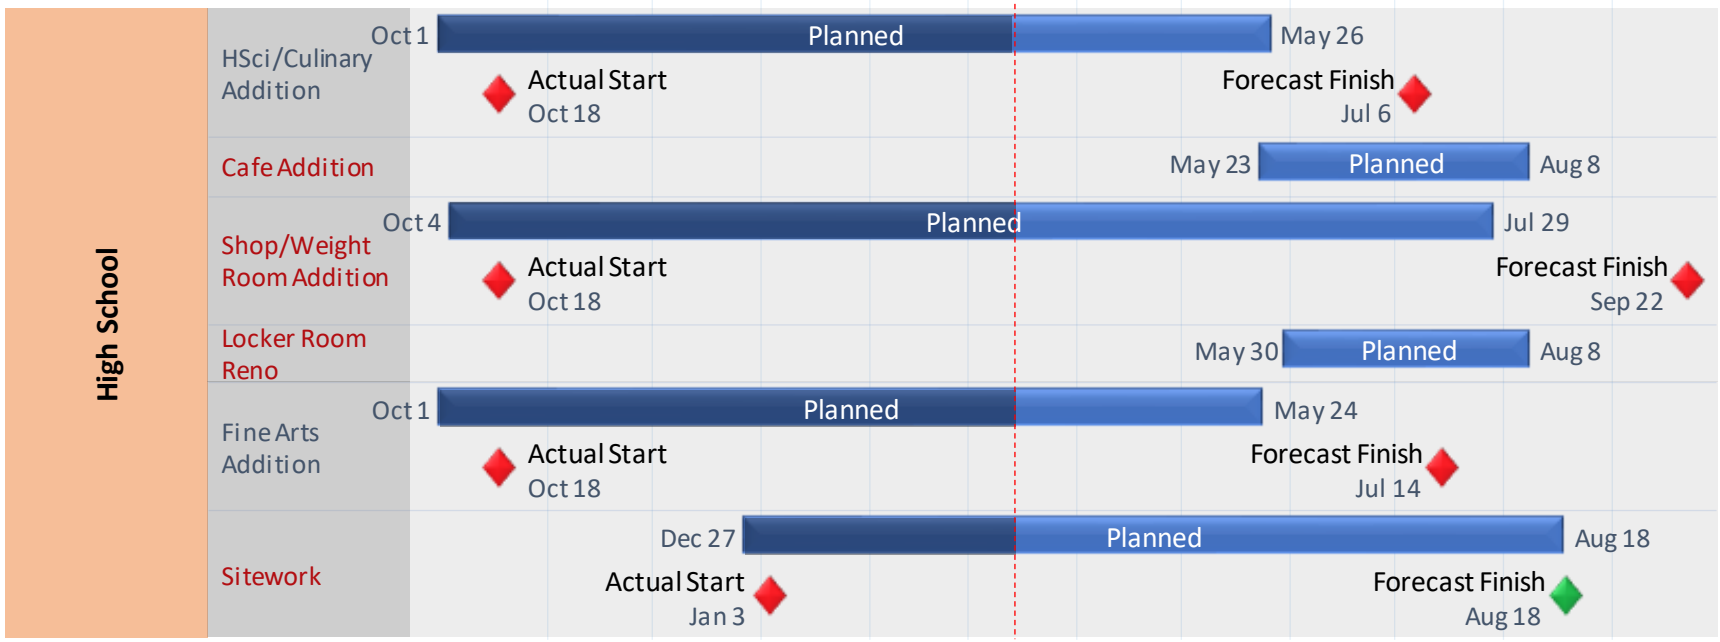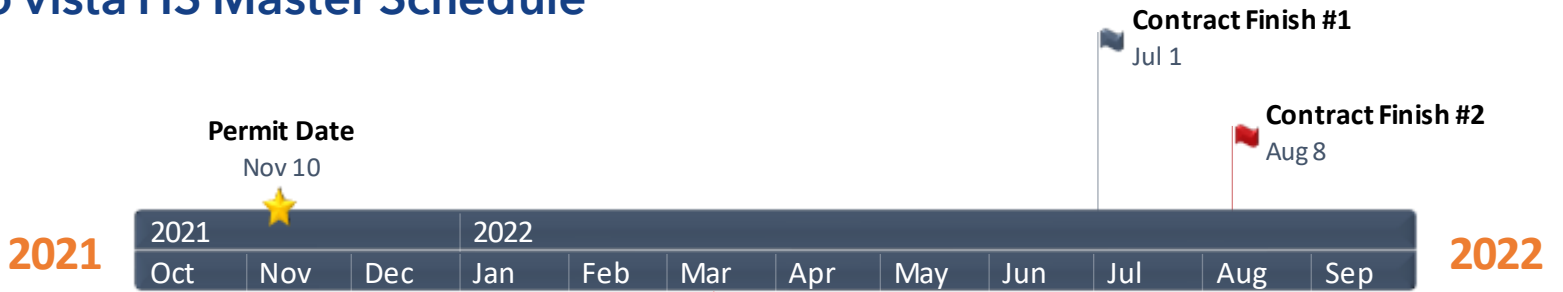

Budget	Committed	Expenditures	Unencumbered
\$11,112,764	\$10,510,452	\$2,205,421	\$602,312



Lago Vista High School Additions

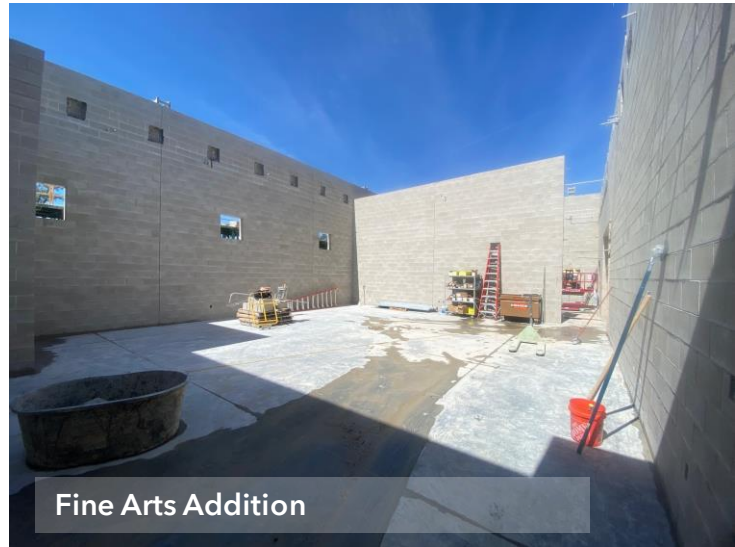




Lago Vista MS Master Schedule

2021



2023

Today

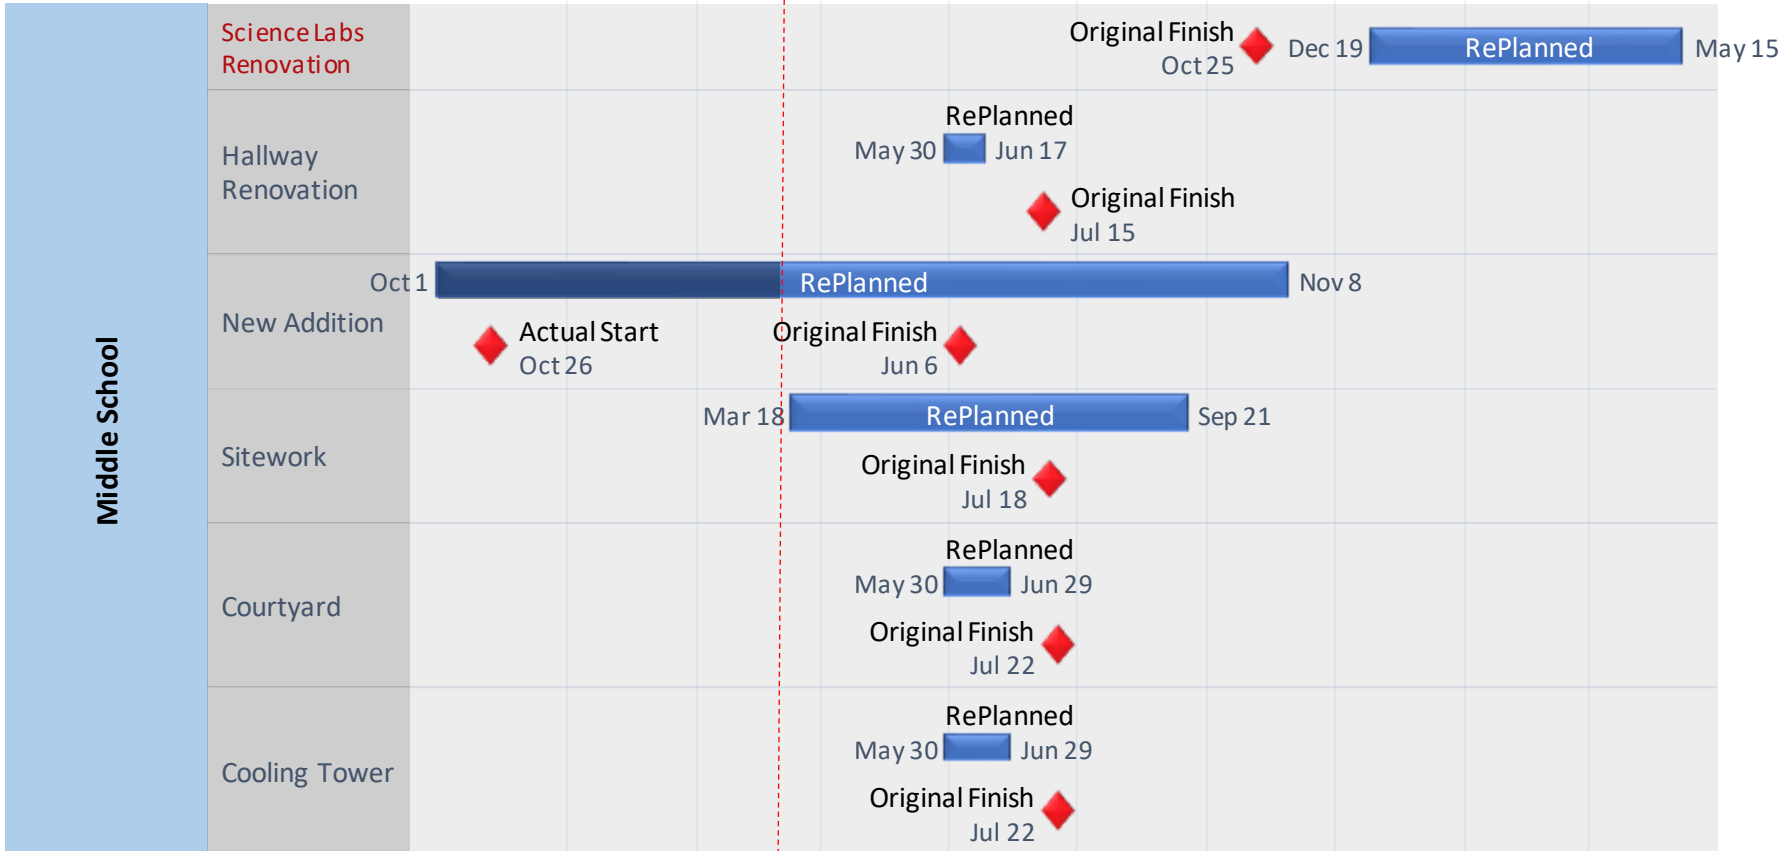

Budget	Committed	Expenditures	Unencumbered
\$8,773,167	\$8,345,973	\$652,048	\$427,194



Lago Vista Intermediate School Conversion

